
ТЕМА №3

З ЧОГО РОЗПОЧАТИ ПРОЕКТ?

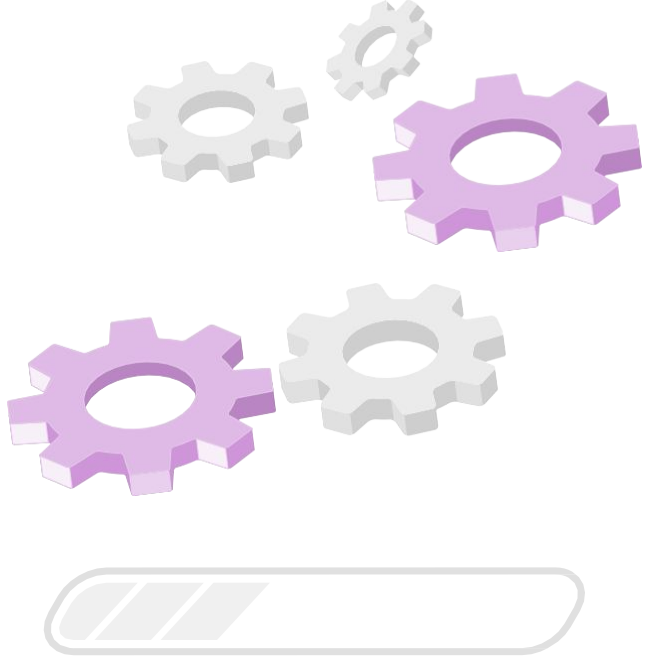


GENIUS space

ОЦІНКА ПРОЕКТУ

Види методів оцінки:

- Оцінка зверху - вниз (Top-down estimation)
- Оцінка знизу - вгору (Bottom-up estimation)
- Трибальна оцінка (Three-point estimation)
- Аналогічна оцінка (Analogous estimation)
- Параметрична оцінка (Parametric estimation)
- Експертна оцінка (Expert judgment)

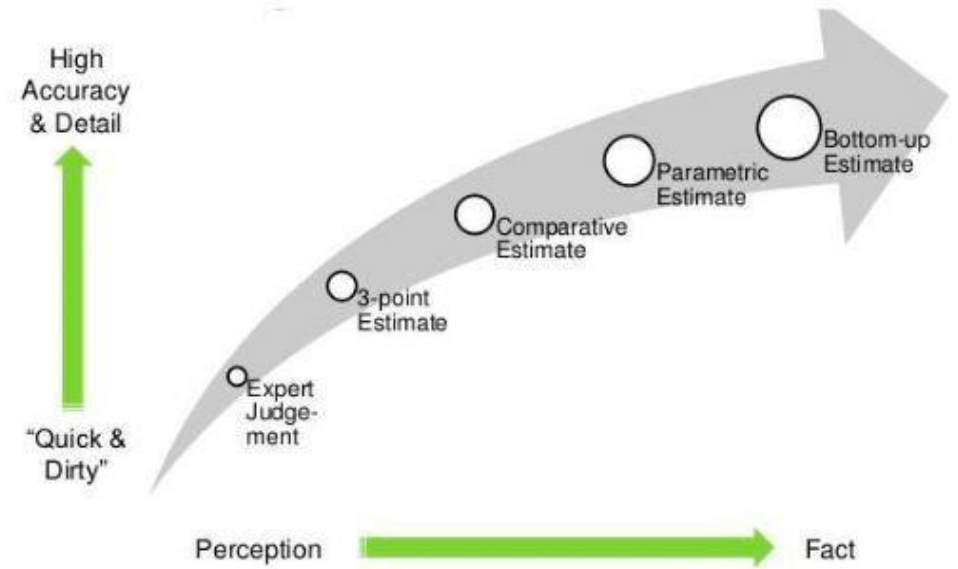

GENIUS space

RFP: ЗАПИТ ПРОПОЗИЦІЇ

RFP

- Формулюйте вимірні бізнес-мети, навіщо робиться ця технологія;
- Формулюйте вимірні завдання, які потрібно зробити для досягнення мети
- Виносьте окремо запит на послуги (підтримка, хостинг, SEO)
- Виносьте окремо запит на роботи (створення продукту, документа, навчання)

За вимогами:

- Виділяйте окремо вимоги до процесу розробки
- Виділяйте окремо вимоги до процесу управління проектом
- Виділяйте окремо функціональні та нефункціональні вимоги
- Виділяйте окремо обмеження

ДОКУМЕНТАЦІЯ

ініціація

- статут проекту
- рішення про запуск
- цілі, масштаб та межі проекту
- затверджений керівник

планування

- залучення до обговорення зацікавлених сторін
- узгодження відповідальності учасників за результати
- бюджет проекту
- уперед / стоп

організація

- робота за планом
- організація
- підбір команди
- управління ризиками

контроль

- тренінги / навчання
- наради, команди
- планування дій
- етапні звіти

завершення

- акт здачі-приймання
- “отримані уроки”
- протокол
- наказ про завершення
- архів проекту

СТАТУТ ПРОЕКТУ (PROJECT CHARTER)

PROJECT CHARTER

Project Title	Project and Portfolio Management Tool			Project Manager	Sameer Patel
Project Start Date	May 21, 2017	Project End Date	August 31, 2017	Project Sponsor	Randy Hadden

Business Need

All Information Technology projects that require agreement on the Memorandum of Understanding between the Customer and the Service Provider are approved through email. This project was initiated to reduce the manual approvals and create a system to obtain and track the approvals to reduce any discrepancies and loss of data.

Project Scope	Deliverables
Create an in-house PPM to include all Global IT projects.	1. Generate consolidated project status report 2. Extract Global Headcount details for all projects
Risks and Issues	**Assumptions/Dependencies**
1. Data discrepancy due to large amount of projects 2. Involvement of multiple teams	1. All Global IT projects to be added to the tool 2. Managers to provide regular updates for the projects

Financials

Budget to complete this project is $3000

Techno-PM
Project Management Templates


Milestones Schedule

Milestone	Target Completion Date	Actual Date
Upload all Global IT Projects to the tool	May 20, 2017	
Complete UAT testing for the tool	July 30,2017	

Project Team		Approval/Review Committee	
Project Manager	Randy Hadden	**Sponsor**	Randy Hadden
Project Manager	Sameer Patel	**Business Division Head**	Aniket Bhonsle
Team Members	Vice President, Senior Manager, Analyst	**Business Unit Head**	Sunil Rajan
		Finance Manager	Ketan Shah

GENIUS space

ПЛАН ПРОЕКТУ (PROJECT PLAN)

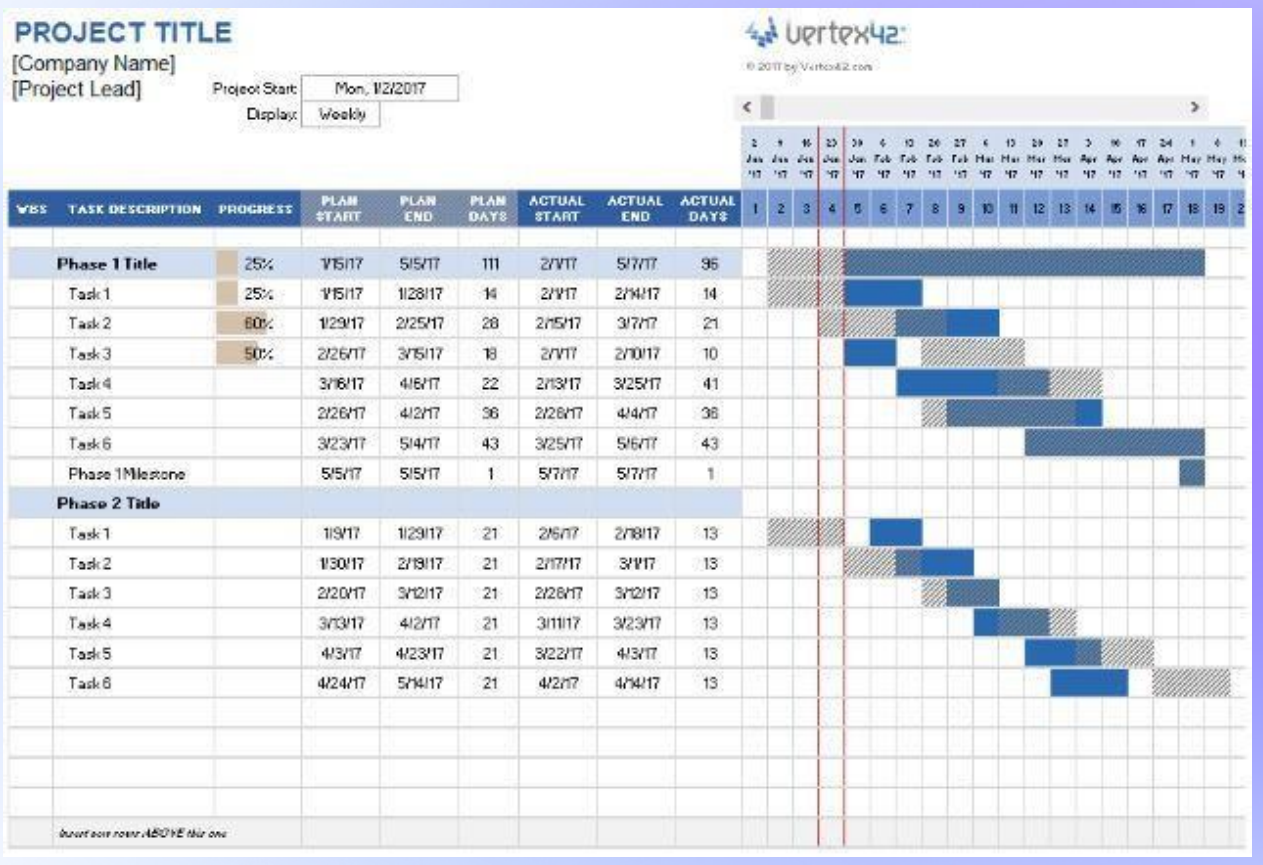

PROJECT TITLE

[Company Name]

[Project Lead]

Project Start: Mon, 1/2/2017

Display: Weekly

vertex42

WBS	TASK DESCRIPTION	PROGRESS	PLAN START	PLAN END	PLAN DAYS	ACTUAL START	ACTUAL END	ACTUAL DAYS
	Phase 1 Title	25%	1/15/17	5/5/17	111	2/1/17	5/7/17	96
	Task 1	25%	1/15/17	1/28/17	14	2/1/17	2/14/17	14
	Task 2	60%	1/29/17	2/25/17	28	2/15/17	3/7/17	21
	Task 3	50%	2/26/17	3/15/17	18	2/1/17	2/10/17	10
	Task 4		3/16/17	4/6/17	22	2/13/17	3/25/17	41
	Task 5		2/26/17	4/2/17	36	2/26/17	4/4/17	36
	Task 6		3/23/17	5/4/17	43	3/25/17	5/6/17	43
	Phase 1Milestone		5/5/17	5/5/17	1	5/7/17	5/7/17	1
	Phase 2 Title							
	Task 1		1/9/17	1/29/17	21	2/6/17	2/18/17	13
	Task 2		1/30/17	2/19/17	21	2/17/17	3/1/17	13
	Task 3		2/20/17	3/12/17	21	2/26/17	3/12/17	13
	Task 4		3/13/17	4/2/17	21	3/11/17	3/23/17	13
	Task 5		4/3/17	4/23/17	21	3/22/17	4/3/17	13
	Task 6		4/24/17	5/14/17	21	4/2/17	4/14/17	13

Insert new rows ABOVE this one



[Company Logo]

[Company Name]

[Project Name]

[Address 1]
[Address 2]
[City, State ZIP]
[Phone]
[Email]
[Contact Name]

Project Manager:
Project Location:
Project Deliverable:
Project Scope:
Start Date:
End Date:

Activities/ Tasks

Sl. No.	Activity/ Task Name	Resource Assigned	Start Date	End Date	Duration (in days)	Activity/ Task Status

GENIUS space

РЕЄСТР ЗАЦІКАВЛЕНИХ ОСІБ (REGISTER OF STAKEHOLDERS)

Stakeholder Register

Project Name	Website Look Redesign			Project Manager	Anthony Daukes			Project Phase	Initiation		Date	5-May-17

Sr. No.	Name	Designation	Department	Role	Contact	Category	Interest	Influence	Expectations	Comms requirements	Comms frequency	Comments
1	John Matthew	Director	Technology	Sponsor	Phone: +61 4834467651 Email: john.matthew@gmail.com	Internal	●●●	●●●	User friendly and responsive UI across handheld device, tablet or desktop	Video Conference and Email	Weekly	
2	Luke Wilson	Vice President	Technology	Project Lead	Phone: +61 4785739580 Email: luke.wilson@gmail.com	Internal	●●●	○●●	Project to be delivered on time within budget	Email and Telephone	Daily	
3	Deepak Patel	Manager	Technology	Product Manager	Phone: +91 9923535534 Email: deepak.patel@gmail.com	Internal	○●●	○○●	Clear Requirements and timely completion of documentation	Email and Telephone	Daily	
4	Suzie Barker	Associate	Technology	PMO	Phone: +65 8542533152 Email: suzie.barker@gmail.com	Internal	○●●	○○●	Project to be delivered on time within budget Timely approvals to be obtained	Email and Telephone	Daily	
5	Thomas Atkins	Vice President	Technology	Dev Manager	Phone: +44 5871512134 Email: thomas.atkins@gmail.com	Internal	○●●	○●●	Develop responsive UI	Email and Telephone	Weekly	
6	Disha Sharma	Vice President	Technology	QA Manager	Phone: +91 9852425634 Email: disha.sharma@gmail.com	Internal	○●●	○●●	UI is responsive No quality issues Branding is maintained	Email and Telephone	Weekly	
7	Jim Arthur	Manager	Technology	Infrastructure Team Lead	Phone: +61 4854665621 Email: jim.arthur@gmail.com	Internal	○●●	○○●	Changes should not affect the uptime of the system No memory spikes	Email and Telephone	Weekly	


●●● High ○●● Medium ○○● Low

GENIUS space

ДОКУМЕНТ ВИМОГ (REQUIREMENTS DOCUMENT)

ID	*Functional Requirement*	*ID*	*Non-functional Requirement*
R.1.	Improving P2P application performance while reducing the network traffic	R.10.	Easy deployment
R.2.	Incentive-compatibility for all player involved	R.11.	Extensibility for new overlay applications
R.3.	Support of different overlay applications	R.12.	Scalability in terms of large end-user population.
R.4.	Interface supporting various optimization schemes	R.13.	Efficiency of the SIS operation
R.5.	QoS support	R.14.	Robustness of the SIS against malicious behavior and against dynamic behavior
R.6.	Different operations: user anonymity mode (free services), user aware mode (premium services)	R.15.	Security: Secure communication between SIS entities and between SIS and overlay application
R.7.	Inter-domain support	R.16.	Standard compliance: The SIS shall use and based on standard protocols where applicable.
R.8.	OAM (Operation and Management) support	R.17.	Transparency: The SIS shall not apply Deep Packet Inspection (DPI).
R.9.	Mobile network support		

ДИЗАЙН ПРОГРАМНОГО ЗАБЕЗПЕЧЕННЯ (DESIGN DOCUMENT)

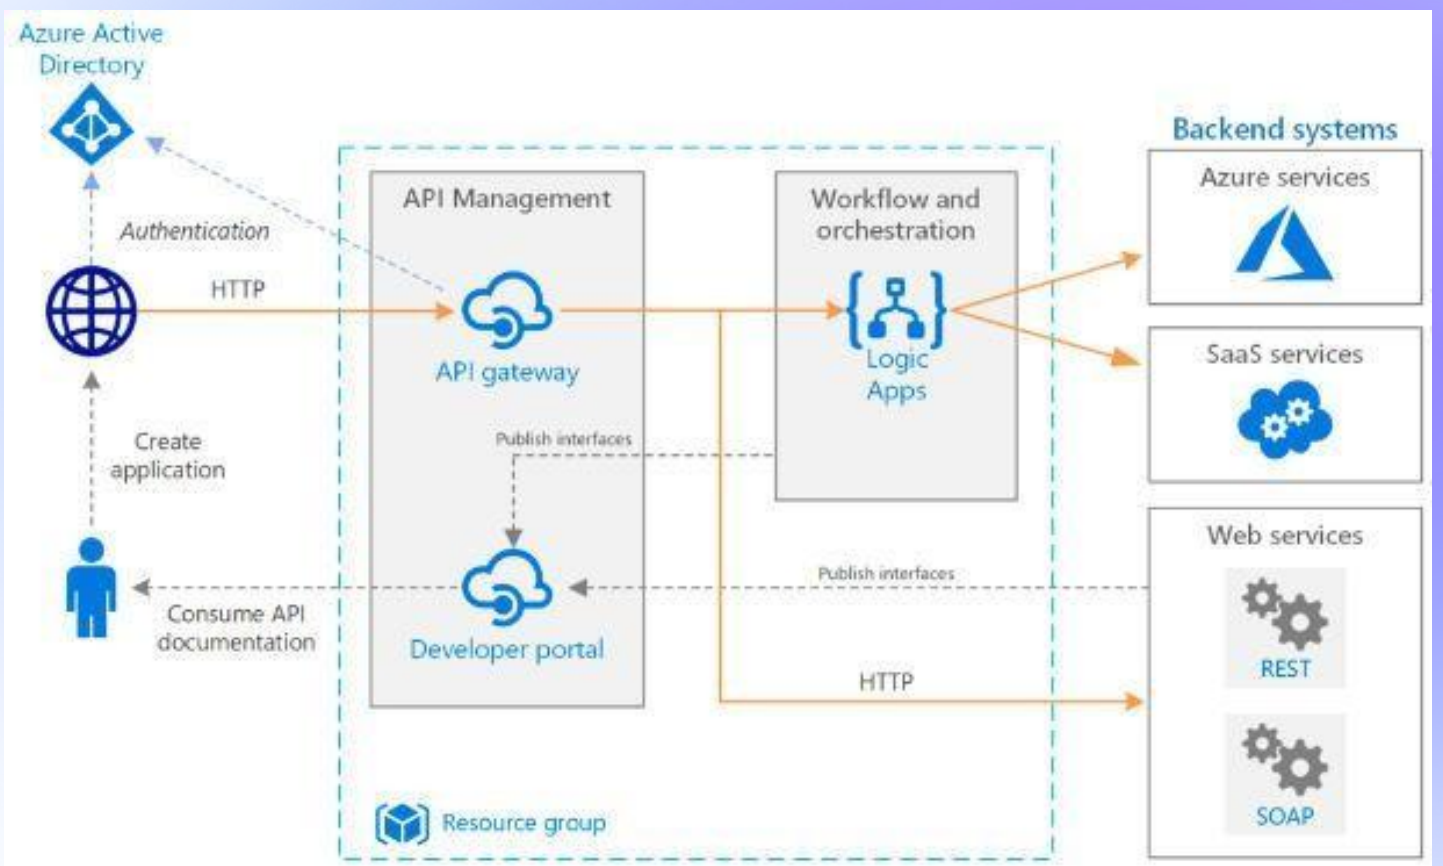

1 Introduction

1.1 Document Scope

Here you should describe what the purpose of this document is, and what it is not (e.g. it does not describe how a user uses the system.) No-one likes to have to read a few pages to figure out if they're looking at the right document.

1.2 Intended audience

This section should describe the stakeholders you are targeting this document at. This is another way to let people quickly discover whether they're reading the wrong document. Hint: in your current assignment, this is not the end-user.

1.3 Project Overview

What is it that you're building? Cross references or links to other documents may be relevant. This is a non-technical overview to provide the right context for understanding the following technical sections.

2 High-Level Design

2.1 Goals and Guidelines

You may adopt either of these two formats:

- Describe the goals and guiding principles ("philosophy") used to design the software, and that affect the architecture and high-level design. Describe the reason for their desirability (if possible, in relation to requirements), unless they are trivially obvious.
- Identify the software requirements and objectives that have a significant impact on the architecture, for example as a bullet list of single line items.

2.2 Architectural Strategies

Describe any design decisions and/or strategies that affect the overall organization of the system and its higher-level structures. How did you approach complicated parts of the design? Did requirements suggest paying special attention to reuse, unattended operation, a certain style or model of user interface, or performance vs memory? UML System Use Case diagrams constituting a high-level use case view may be useful to explain or justify your approach, but are not mandatory. Show only Use Case diagrams which depict significant, central functionality of the final system, or that have an architectural impact. Examples:

- Database. How is data storage management and persistence handled?
- Communication mechanisms, for example between components
- Expansion. Are there future plans for extending or enhancing the software? Will you leave interfaces for future expansion, 3rd party additions, etc.?
- Data Management. Are data items being transferred between subsystems or imported into/exported from your application tagged with a format version number in case future releases of the application change the transmission format?

РЕЄСТР РИЗИКІВ (RISK MANAGEMENT PLAN)

RISK MANAGEMENT MATRIX

NAME		OBJECTIVE	

REF / ID	PRE-MITIGATION				DEPARTMENT / LOCATION	MITIGATIONS / WARNINGS / REMEDIES	POST-MITIGATION			
	RISK	RISK SEVERITY	RISK LIKELIHOOD	RISK LEVEL			RISK SEVERITY	RISK LIKELIHOOD	RISK LEVEL	ACCEPTABLE TO PROCEED?
		- ACCEPTABLE - TOLERABLE - UNDESIRABLE - INTOLERABLE	- IMPROBABLE - POSSIBLE - PROBABLE	- LOW - MEDIUM - HIGH - EXTREME			- ACCEPTABLE - TOLERABLE - UNDESIRABLE - INTOLERABLE	- IMPROBABLE - POSSIBLE - PROBABLE	- LOW - MEDIUM - HIGH - EXTREME	YES / NO

TEST PLAN

6.1.1.1 Add server command

ID	TC-R1
Description	Add an additional server to test redundancy.
Precondition	A target server is configured, turned on, and ready to be added.
Action	The admin user runs the command to add a server to the list of available servers while on an existing server.
Expected Result	The target server is added to the list of servers and all clients and other servers are notified.
Failure Condition	1. The target server is not added to the list of servers. 2. No clients or servers are notified.

6.1.1.2 Checking Data While No Data is Being Manipulated

ID	TC-R2
Description	Ensure all data is consistent between all current servers and the newly added server. While the check is happening no data is being manipulated by other users.
Precondition	A target server is configured, turned on, and an existing server had added the target.
Action	The server which was told by the administrator to add a target server ensures all data between the two servers are identical.
Expected Result	The target server has an identical data set to all other servers.
Failure Condition	1. The target server does not have all data. 2. The target server data is not identical.

6.1.1.3 Checking Data While Data is Being Manipulated

ID	TC-R3
Description	Ensure all data is consistent between all current servers and the newly added server. While the check is happening data is being modified on the server.

7. Test Strategy

7.1. Test level responsibility

Detail the testing levels expected to be applied and who has primary (P) and secondary (S) responsibility for performing this testing (example below).


Test Level	External Party	Proj Team	Business
Unit Testing		P	
Integration Testing		P	
Security Testing	P	S	
Connectivity Testing		P	
User Acceptance Testing		S	P
Production Verification Testing		S	P

7.2. Test Type & Approach

Detail the types of testing covered by the project team and their standard objectives (example below)

Test Type	Objectives
Progression Requirements	The objectives are to verify that the application: • Meets the defined requirements; • Performs and functions accurately; • Correctly handles error conditions; • Interfaces function correctly; • Data load is successful. Functional testing will occur in an iterative and controlled manner, ensuring the solution matches the defined requirements.
Regression testing	

USER & MAINTENANCE MANUALS

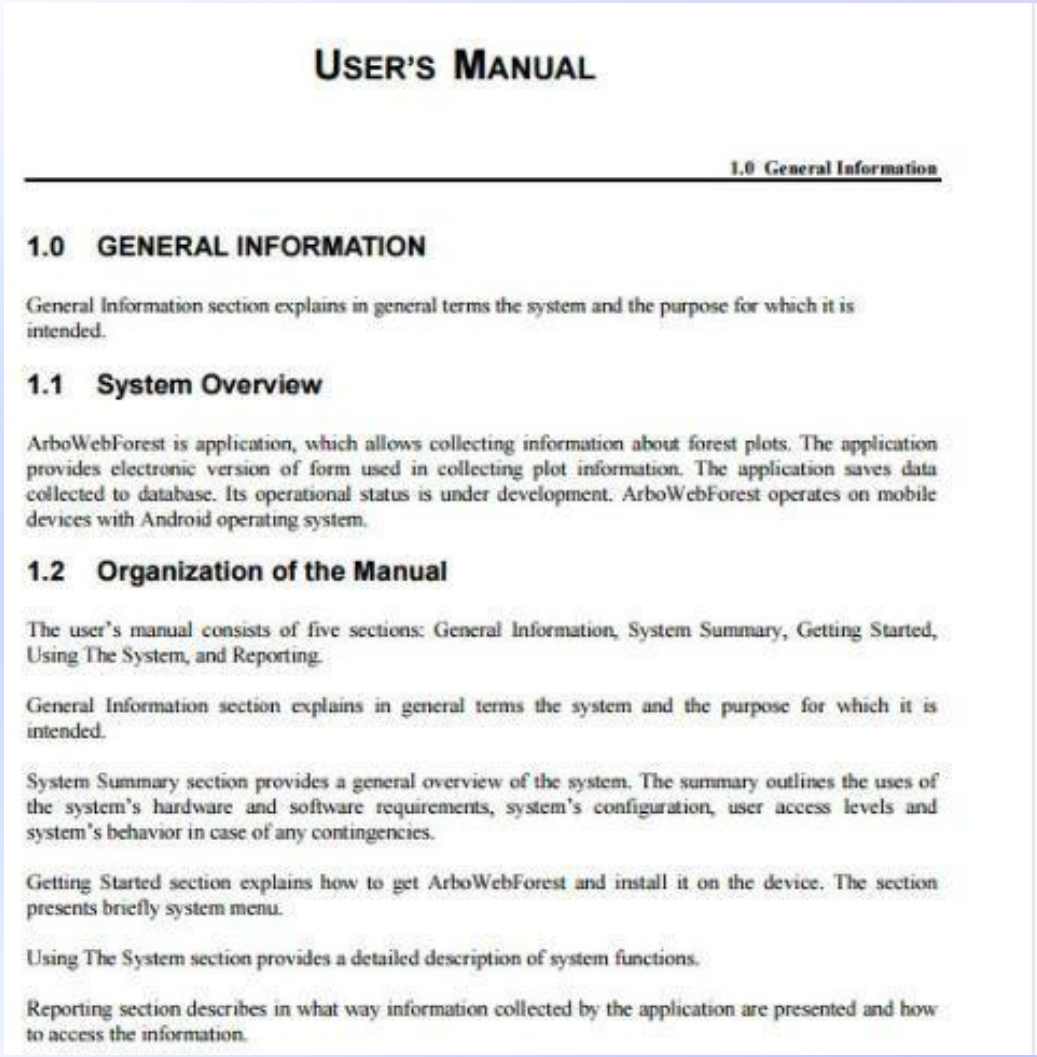

USER'S MANUAL

1.0 General Information

1.0 GENERAL INFORMATION

General Information section explains in general terms the system and the purpose for which it is intended.

1.1 System Overview

ArboWebForest is application, which allows collecting information about forest plots. The application provides electronic version of form used in collecting plot information. The application saves data collected to database. Its operational status is under development. ArboWebForest operates on mobile devices with Android operating system.

1.2 Organization of the Manual

The user's manual consists of five sections: General Information, System Summary, Getting Started, Using The System, and Reporting.


General Information section explains in general terms the system and the purpose for which it is intended.

System Summary section provides a general overview of the system. The summary outlines the uses of the system's hardware and software requirements, system's configuration, user access levels and system's behavior in case of any contingencies.

Getting Started section explains how to get ArboWebForest and install it on the device. The section presents briefly system menu.

Using The System section provides a detailed description of system functions.

Reporting section describes in what way information collected by the application are presented and how to access the information.

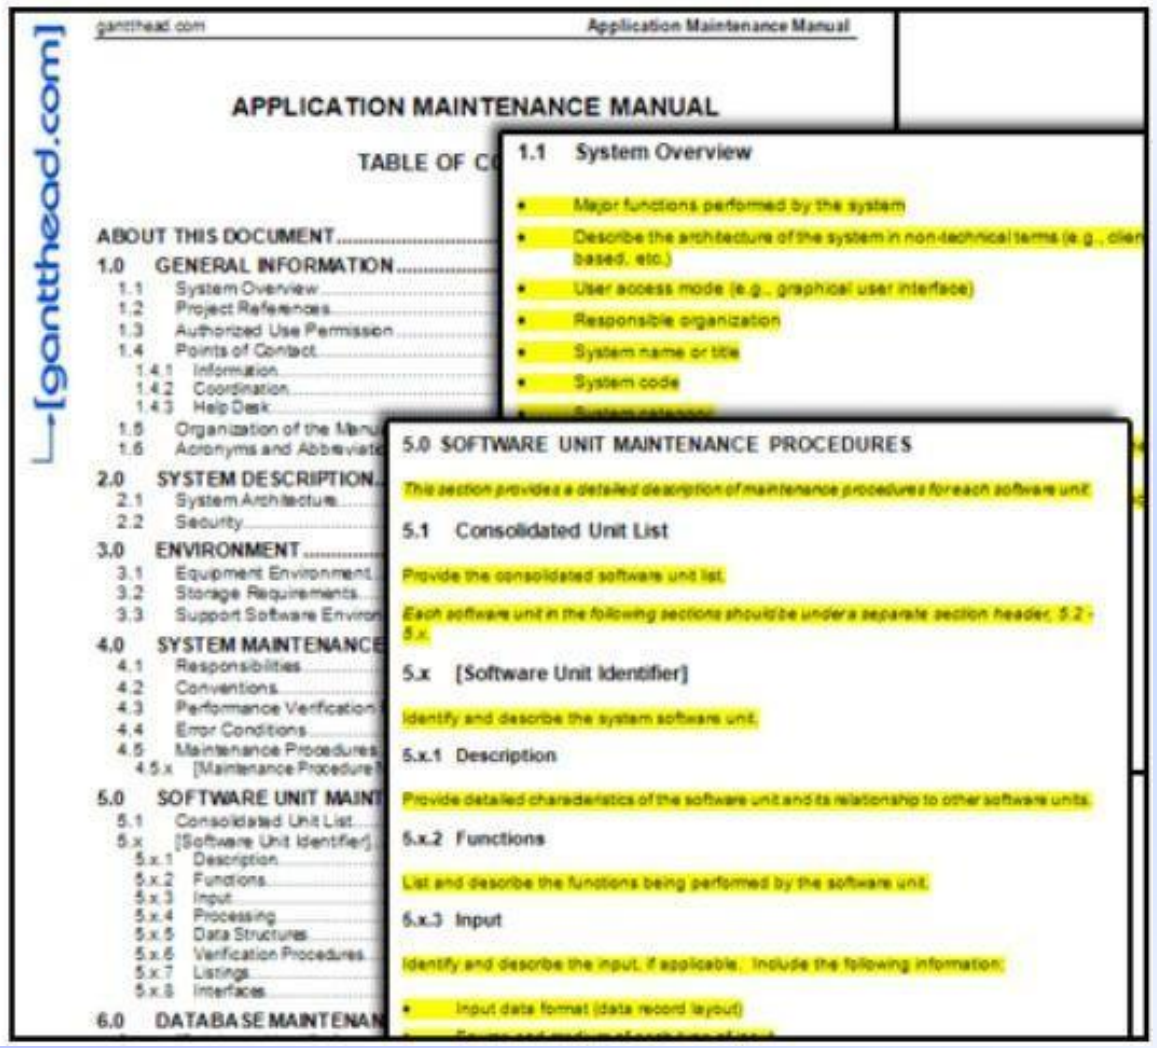

[ganthead.com]

ganthead.com Application Maintenance Manual

APPLICATION MAINTENANCE MANUAL

TABLE OF C

ABOUT THIS DOCUMENT
1.0 GENERAL INFORMATION
1.1 System Overview
1.2 Project References
1.3 Authorized Use Permission
1.4 Points of Contact
1.4.1 Information
1.4.2 Coordination
1.4.3 Help Desk
1.5 Organization of the Manu
1.6 Acronyms and Abbreviati
2.0 SYSTEM DESCRIPTION
2.1 System Architecture
2.2 Security
3.0 ENVIRONMENT
3.1 Equipment Environment
3.2 Storage Requirements
3.3 Support Software Environ
4.0 SYSTEM MAINTENANCE
4.1 Responsibilities
4.2 Conventions
4.3 Performance Verification
4.4 Error Conditions
4.5 Maintenance Procedures
4.5.x [Maintenance Procedure]
5.0 SOFTWARE UNIT MAINT
5.1 Consolidated Unit List
5.x [Software Unit Identifier]
5.x.1 Description
5.x.2 Functions
5.x.3 Input
5.x.4 Processing
5.x.5 Data Structures
5.x.6 Verification Procedures
5.x.7 Listings
5.x.8 Interfaces
6.0 DATABASE MAINTENAN

1.1 System Overview

- Major functions performed by the system
- Describe the architecture of the system in non-technical terms (e.g., clien based, etc.)
- User access mode (e.g., graphical user interface)
- Responsible organization
- System name or title
- System code

5.0 SOFTWARE UNIT MAINTENANCE PROCEDURES

This section provides a detailed description of maintenance procedures for each software unit.

5.1 Consolidated Unit List

Provide the consolidated software unit list.

Each software unit in the following sections should be under a separate section header, 5.2 - 5.x.

5.x [Software Unit Identifier]

Identify and describe the system software unit.

5.x.1 Description

Provide detailed characteristics of the software unit and its relationship to other software units.

5.x.2 Functions

List and describe the functions being performed by the software unit.

5.x.3 Input

Identify and describe the input, if applicable. Include the following information:

- Input data format (data record layout)

PROJECT STATUS REPORT



Project's Name: Status W#1 2023

Created by Mariaryna Bobodilova
Just a moment ago · 1 min read · Analytics

⚠ **Confidential:** This is INTERNAL ONLY information and should not be shared outside the company.

- EXECUTIVE SUMMARY
- PROJECT HEALTH
  - PROJECT ISSUES
- DEPENDENCY TRACKER
- THIRD-PARTY INTEGRATIONS
- CURRENT SPRINT HEALTH
- - Insert screenshot from Jira
- UPCOMING DATES / EVENTS
- Report Recipients:


Project	Name
Reporting period	2023-W1
Global Status	MODERATE RISK
Sprint Status	MODERATE RISK

EXECUTIVE SUMMARY

- Target Scope Burndown vs timeline: 0% VS 0%
- Target Scope Burndown vs budget: 0% VS 0%
- Target Scope Confidence: (0% - 50% red, 51% - 80% yellow, 81% + green) 0%
- Remaining Team CAPA vs remaining target scope: - 0 PD / 0 PD

PROJECT HEALTH

On-Time		On Budget		In Quality
Burned Target scope vs. Planed Scope in (in PD) - GROSS	N/A	Team Est. vs. Sales Est.	N/A	Backlog Readiness
Remaining scope until planed release (in PD) - GROSS	N/A	Spent + Remaining vs Team Est.	N/A	Issues Resolved VS Issues Planned (Sprint)
Target Scope changes (-/+) in PD	N/A	Spent + Remaining vs. Sales Est.	N/A	Time Spent for Bugs vs Development Time (Sprint)
				Average Hours Spent Per Bug (Sprint)
				Bugs Resolved vs Created (Sprint)

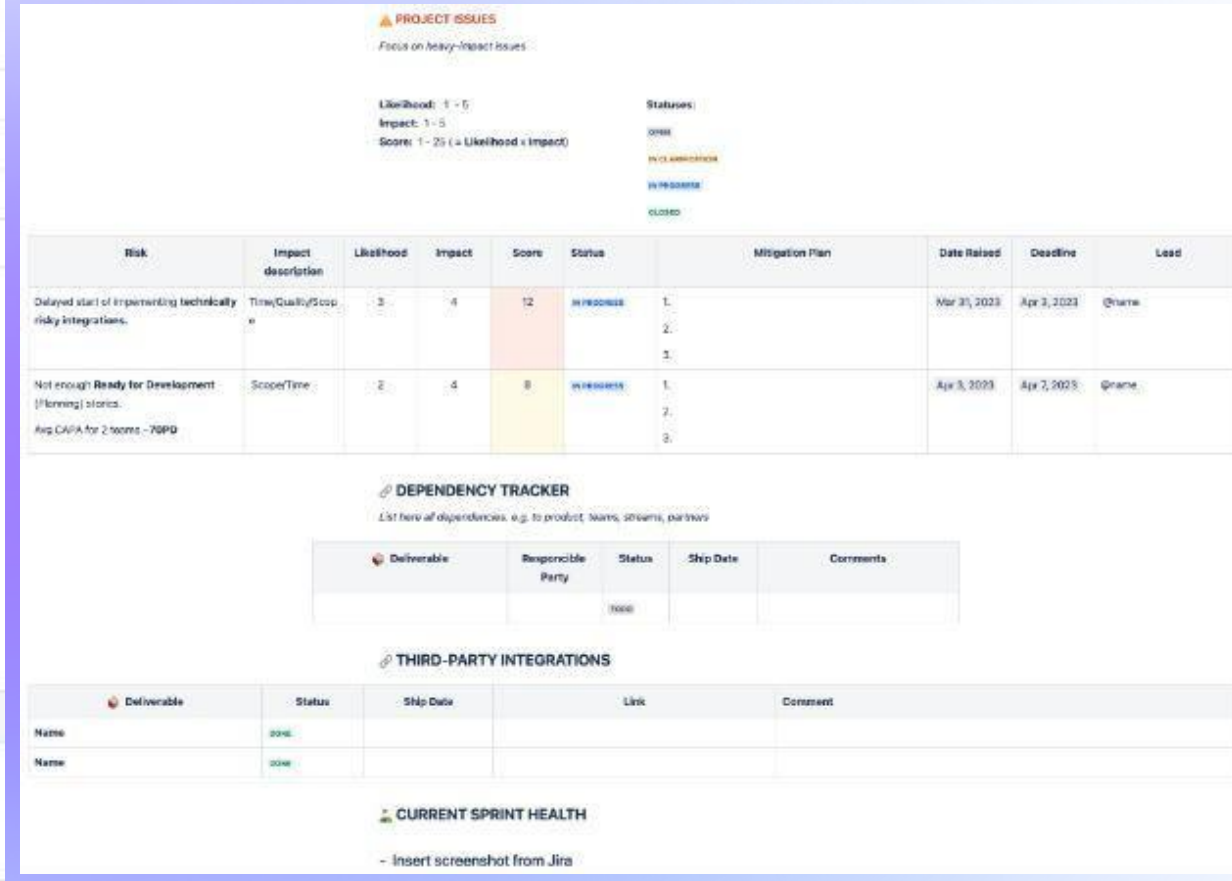

PROJECT ISSUES

Focus on heavy-impact issues

Likelihood: 1 - 5
Impact: 1 - 5
Score: 1 - 25 (= Likelihood x Impact)

Statuses:
OPEN
IN CLARIFICATION
IN PROGRESS
CLOSED

Risk	Impact description	Likelihood	Impact	Score	Status	Mitigation Plan	Date Raised	Deadline	Lead
Delayed start of implementing technically risky integrations.	Time/Quality/Scope	3	4	12	IN PROGRESS	1. 2. 3.	Mar 31, 2023	Apr 3, 2023	@name
Not enough **Ready for Development** [Planning] stories. Avg CAPA for 2 teams - 70PD	Scope/Time	2	4	8	IN PROGRESS	1. 2. 3.	Apr 3, 2023	Apr 7, 2023	@name

DEPENDENCY TRACKER

List here all dependencies, e.g. to product teams, streams, partners

Deliverable	Responsible Party	Status	Ship Date	Comments
		NEW		

THIRD-PARTY INTEGRATIONS

Deliverable	Status	Ship Date	Link	Comment
Name	DONE			
Name	DONE			

CURRENT SPRINT HEALTH

- Insert screenshot from Jira

GENIUS space

IF YOU ARE GOING TO SIN, SIN AGAINST GOD, NOT THE BUREAUCRACY. GOD WILL FORGIVE YOU BUT THE BUREAUCRACY WON'T.

(HYMAN G. RICKOVER)

GENIUS space

ДОДАТКОВІ МАТЕРІАЛИ

- Оцінювання проєкту: власний досвід та висновки
- Навіщо дотримуватися документування на проєкті і хто це повинен контролювати
- Key Project Documents Every Project Manager Needs - Templates



Книга "Мистецтво управління IT-проектами" — Скотт Беркун
